

Construction of a building complex (Academic building, Admin building & Canteen building)
for the Faculty of Allied Health Science, University of Ruhuna; Walahanduwa, Galle



Actual Physical Progress as @ 27th August 2021 – 36%

Date of Commencement – 3rd December 2020

Proposed Date of Completion – 3rd June 2023

Initial Contract price - Rs. 1,501,729,599.71 + VAT


Financial work done – Rs. 530,217,005.25

Outstanding bills – **Rs. 49,603,613.28**

Physical progress

Building A – Academic Building (6 Storied)

- ✓ Foundation Concreting works – 100%
- ✓ Ground floor columns – 100%
- ✓ Ground floor brick works - 80
- ✓ 1st floor Slabs & Columns – 100%
- ✓ 2nd floor Slab – 100%
- ✓ 2nd floor Columns – 20%

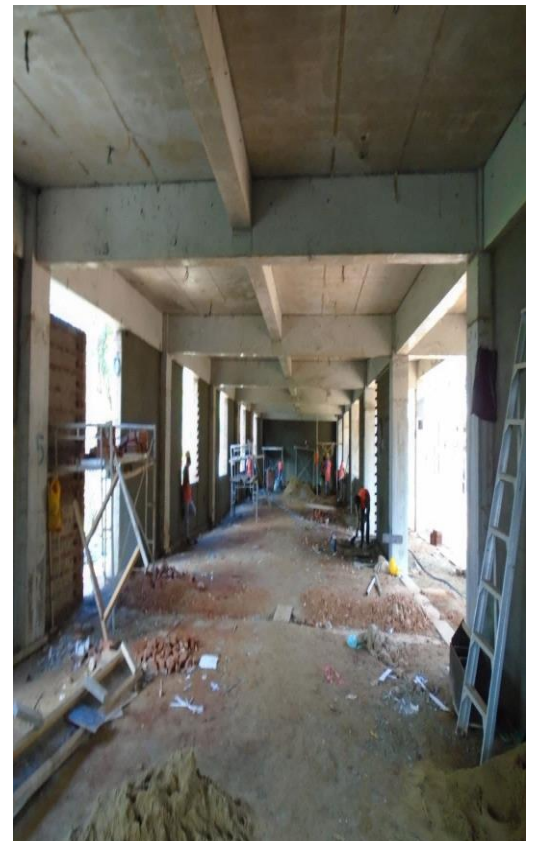

Building B – Administrative & Library Building (3 Storied)

- ✓ Foundation Concreting works – 100%
- ✓ Ground floor columns – 100%
- ✓ 1st floor Slabs - 20%



Building C – Canteen & Common Building (2 Storied)

- ✓ Footing excavation, screeding & base concreting – 30%



Issues and Concerns

- **Contractor repeatedly expresses the difficulty of the access road for their transportation matters.**
